




Interstate 405 Improvement Project Update

Huntington Beach City Council



Project Location and Key Features

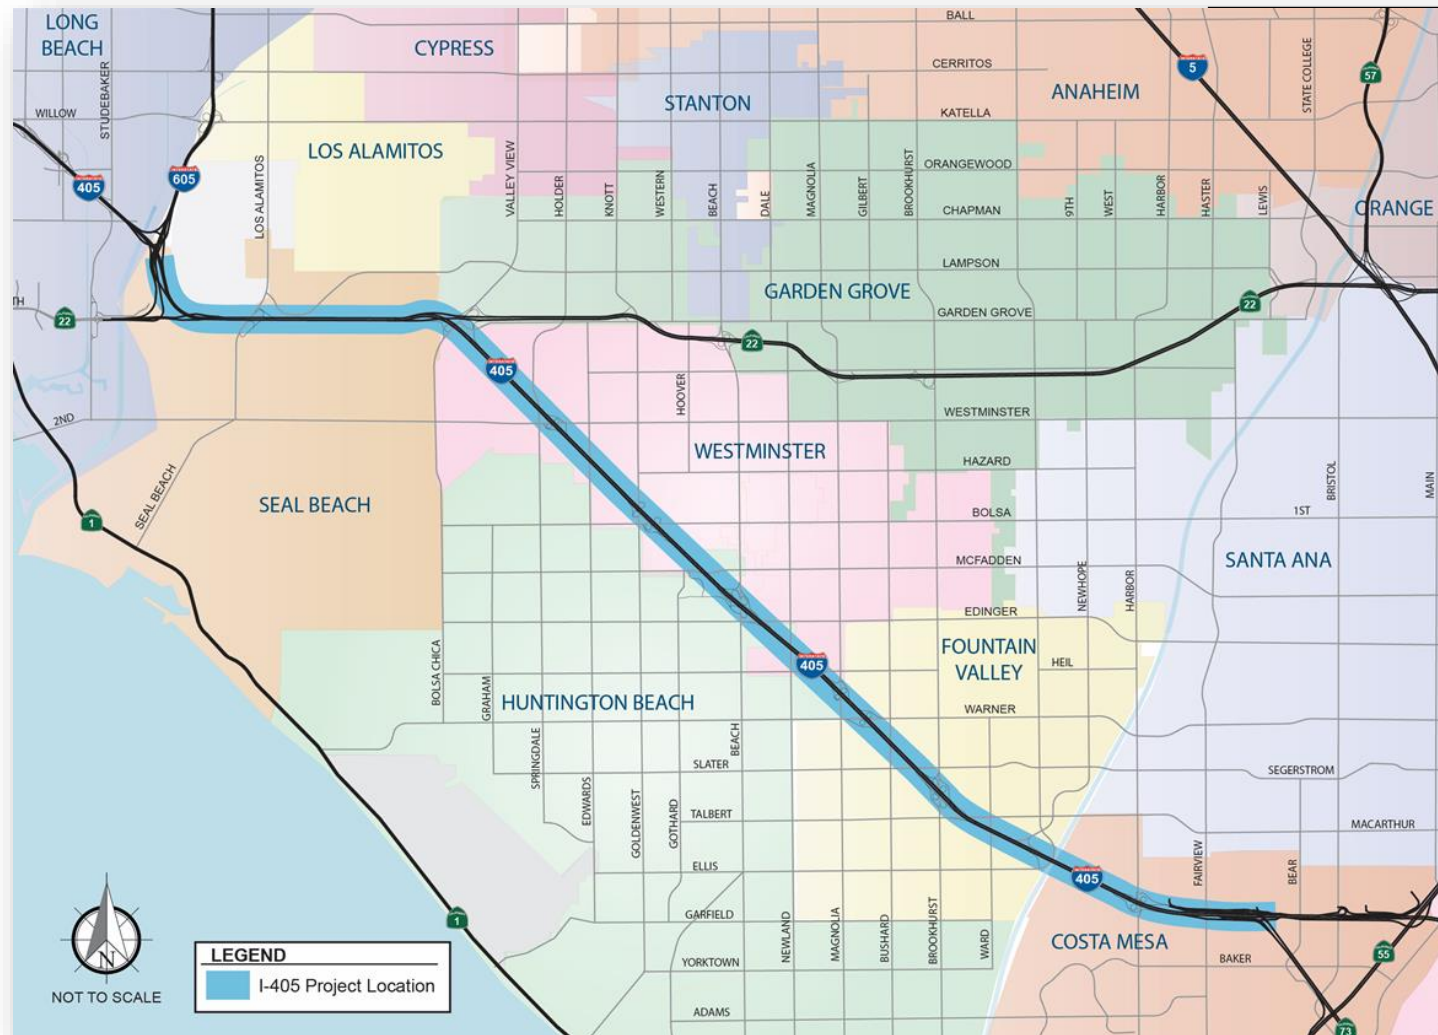

Background



Milestone	Completion Date
Environmental clearance	May 2015
Orange County Transportation Authority Board of Directors awards design-build (DB) contract to OC 405 Partners	November 2016
Notice to Proceed (NTP) No. 1 issued	January 2017
NTP No. 2 issued	July 2017
Construction began	March 2018
Anticipated substantial completion	Late 2023

Construction Update



Talbert Avenue bridge construction



Bushard Street bridge complete

Construction Update



Magnolia Street bridge construction



**Heil Avenue pedestrian
overcrossing construction**

Construction Update



Edinger Avenue bridge construction

Construction Update



Beach Boulevard construction

Construction Update



McFadden Avenue bridge complete

Construction Update



Bolsa Avenue bridge construction



Goldenwest Street bridge construction



Edwards Street bridge construction



Bolsa Chica Road bridge construction

Bridge Construction Map



Engagement Strategies



Print

- Door-to-door canvassing
- Mailers
- Advertising

Digital


- Email Blasts
- Interactive Map
- Social Media
- Project Website

Mobile

- Helpline (English, Español, Tiếng Việt)
- Call/Text Alerts
- Location-based advertising
- Project App
- Waze

Virtual Face-to-Face

- Neighborhood Meetings
- Business Outreach
- Speakers Bureau
- Community Events

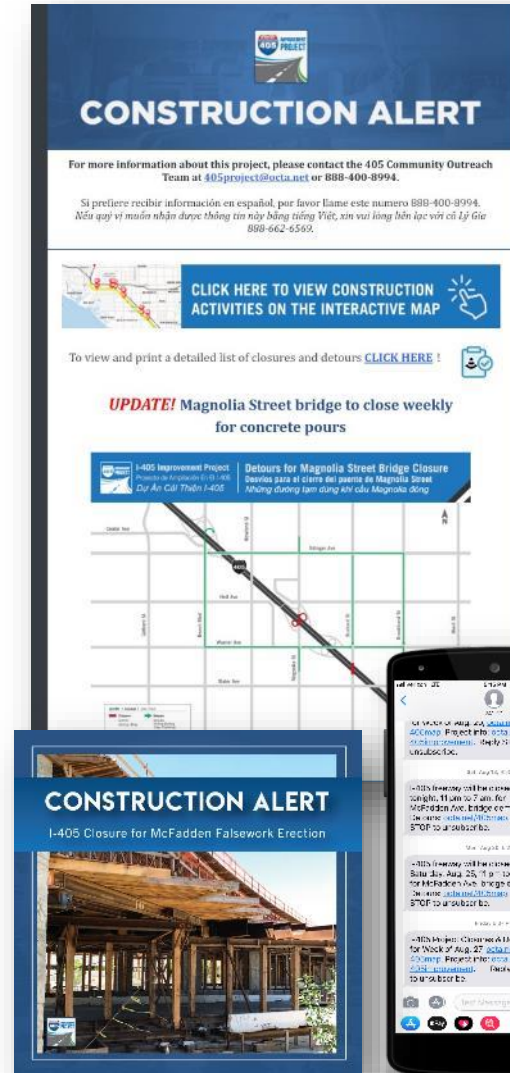

Upcoming Outreach



- Neighborhood Meetings
 - Beach Boulevard Update – Spring
 - Bolsa Avenue Phase 2 – Summer
 - Warner Avenue – Summer
 - Edinger Update – Fall
- Milestones
 - Magnolia Bridge Completion
- Key Stakeholder Briefings
 - Emergency responders
 - School districts
 - Major employers
 - Diverse, disadvantaged communities

ONLINE MEETING

 **NEIGHBORHOOD MEETING**
Edinger Avenue Bridge Construction Update

4 TO 5 P.M. THURSDAY, SEPT. 17, 2020

CLICK TO JOIN MEETING

Visit bit.ly/405webinar-anawood at 4 p.m. Thursday to join the online meeting.



